



ENGINEERING SUCCESS **TOGETHER**

WEEKLY SUMMARY REPORT

Client:	Needham DPW	Dates:	04/15/2017 to 04/21/2017
Contract:	Downtown Improvements	Inspector on site:	D.K.
Contractor:	MDR Construction Co., Inc.		

WORK COMPLETED THIS WEEK

- Completed installation of the street light poles and luminaires
- Began connecting the wiring of the luminaires to the lighted bollards
- Continuing to modify traffic signal settings and cycles as required
- Began construction of the brick masonry wall on the west side of the Common

WORK ANTICIPATED FOR NEXT WEEK

- All work scheduled to take place during the day
- Continue connecting the wiring of the luminaires to the lighted bollards
- Complete the installation of the camera and telemetry wiring to Town Hall (not begun to date)
- Begin the construction of the foundations for future kiosk, statue and fountain (not begun to date)
- Continue the construction of the brick masonry wall at the entrance to the common
- Begin installation of the structural soil associated with the future tree plantings in sidewalk areas (not begun to date)
- Continue shop drawing submissions and processing

BETA GROUP, INC.

315 Norwood Park South, 2nd Floor, Norwood, MA 02062

P: 781.255.1982 | F: 781.255.1974 | W: www.BETA-Inc.com



Connecting wiring to luminaires on lighted bollards on the southwest corner of Chestnut St and Great Plain Ave




Installing brick masonry wall on the west side of the Common entrance

Needham DPW
Downtown Improvements



Rear of brick masonry wall being constructed on the west side of the Common entrance

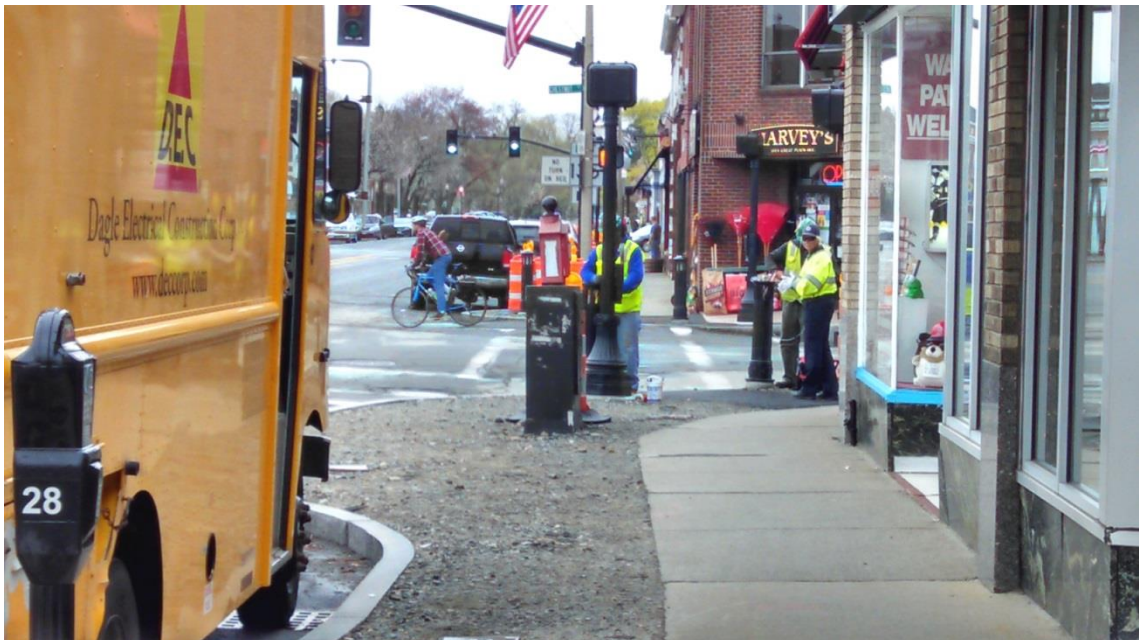

Subcontractor installing luminaires on lighted bollards on the northwest corner of Great Plain Ave and Chestnut St
