

WORK ANTICIPATED FOR NEXT WEEK

- Rock drilling of proposed roadway and lots
- Blasting of proposed roadway and lots
- Excavation of blasted rock and hauling to alternate onsite location
- Stone masons to continue building retaining walls
- Delivery of pipe bedding materials
- Street excavation to connect existing utilities, such as drainage, water and sewer


PHOTOS



Hauling operations completed 10/27/15



BCME Blasting on site and blasting begins 10/27/15

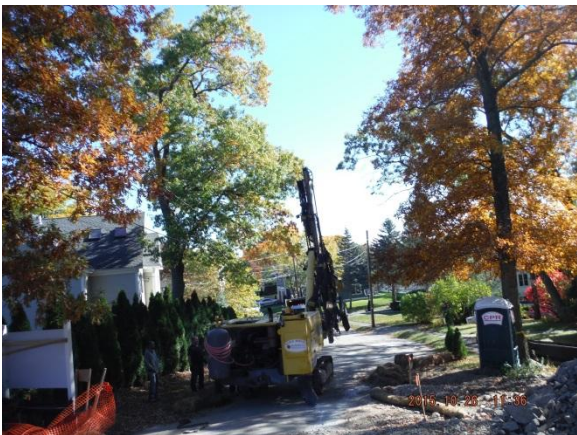

Drill rig probing for ledge Rockwood Lane 10/27/15



Set blasting mats 10/27/15

Needham DPW
Rockwood Lane Extension



Charges being set for blasting 10/27/15



Blasted rock loaded and moved to alternate onsite location 10/26/15
